



FOWLERVILLE COMMUNITY SCHOOLS



Fowlerville K-2 Elementary: Project Activities

- BCC and BFS has approved all disciplines.
- Steel joists and decking are completed. Roofing continued on the west side of the building.
- Sand laid on the west side of the building in preparation for interior flatwork.
- Duct, fire suppression, interior plumbing and electrical continues around the building.
- The construction team is in conversation with DTE and Consumer's Energy to finalize service to the new building.
- All long lead items appear to still be on track. Boilers, pumps, RTUs, and VUVs have been received. Lead times are updated weekly and are reflected in the construction schedule.

Construction Change Documents:

- Bulletin #11 was issued on November 28, 2023 to clarify the flagpole location and add brick relief brackets at the bump outs.
- Bulletin #12 was issued on December 22, 2023 to incorporate RFI responses, revise the details for the columns at the west side of the building, and add a plaster trap to the art room.

Schedule Status – Look Ahead:

- Interior flatwork to begin mid-January.
- Roofing to continue into early February.

Miscellaneous:

- A training as part of the AGC MIOSHA Alliance Program will be held Spring of 2024.


Project Progress Photographs



Sand being delivered to job site for interior flatwork.




Sand being loaded into the slinger in order for it to be shot into building.

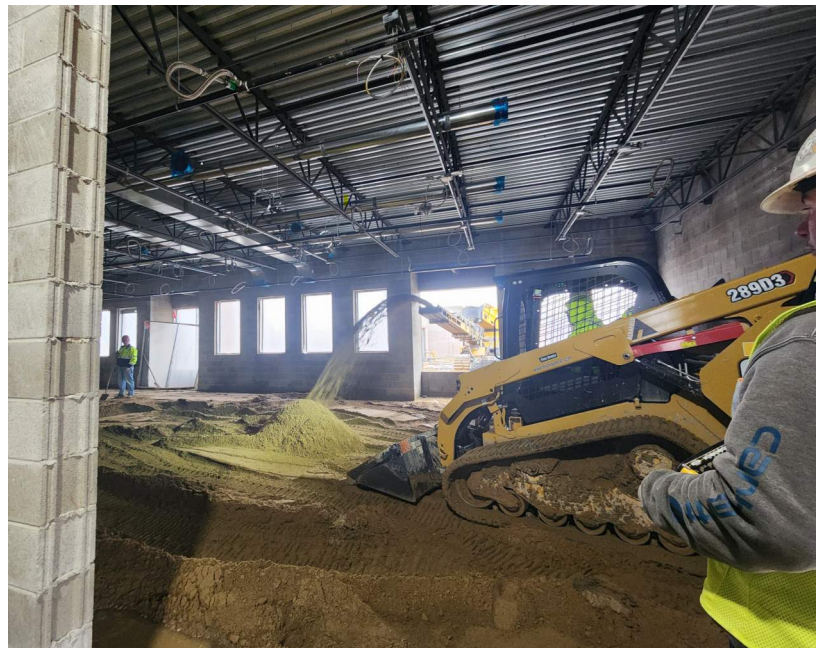

Sand being shot into the building and spread by a skid steer.

Project Progress Photographs

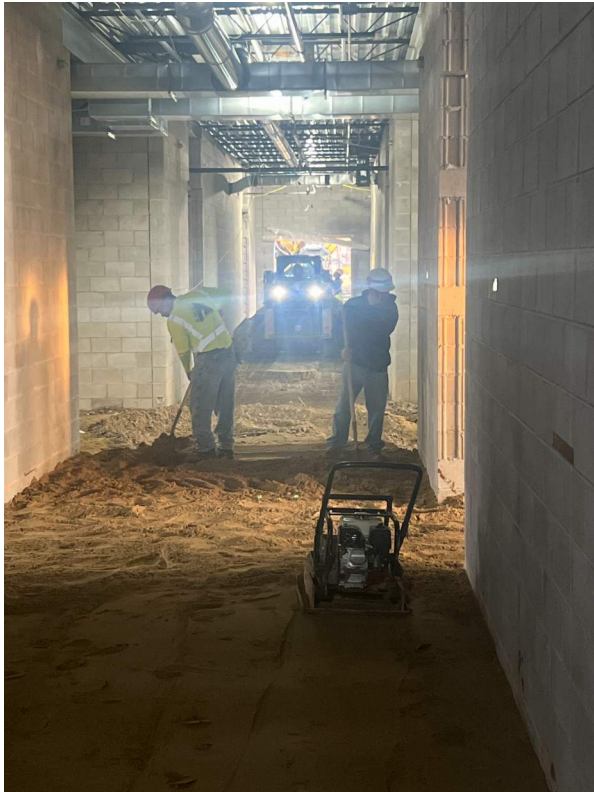

Spreading of sand in the hallway.



Staged roofing materials.




Roofing in progress and warning lines installed.

Project Progress Photographs



Underground conduit in progress.

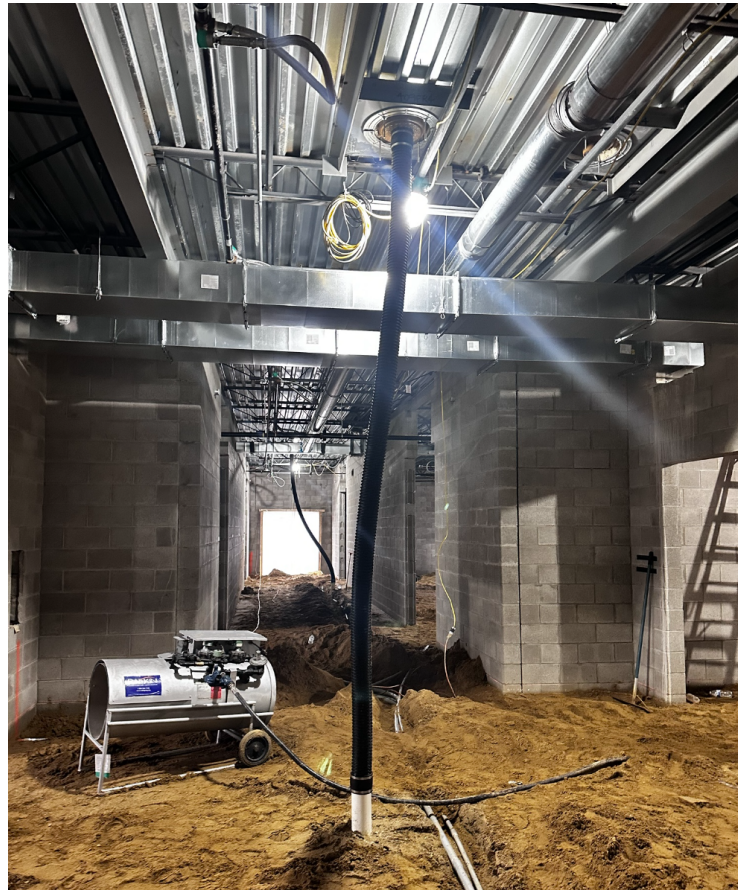

Roof drain connection to keep sand dry.
