



# FOWLERVILLE COMMUNITY SCHOOLS



## **Fowlerville K-2 Elementary: Project Activities**

- BCC and BFS has approved all disciplines.
- Roofing is in progress on the east side of the building.
- Interior flatwork began on the west side of the building.
- Column framing was completed on the east side of the building in preparation for brick.
- Classroom entryway masonry and door frame install are in progress.
- Duct, fire suppression, interior plumbing and electrical continues around the building.
- The construction team is in conversation with DTE and Consumer's Energy to finalize service to the new building.
- All long lead items appear to still be on track. Boilers, pumps, RTUs, and VUVs have been received. Lead times are updated weekly and are reflected in the construction schedule.

## **Schedule Status – Look Ahead:**

- Roofing to continue into mid-February.
- Window install to begin in mid-February.

## **Miscellaneous:**

- A training as part of the AGC MIOSHA Alliance Program will be held Spring of 2024.

## **HVAC Project Planning:**

- The High School and Junior High HVAC project documents were issued for bids on January 10, 2024
- The pre-bid meetings for both the High School and Junior High were held on January 17, 2024.
- Bids for both projects are due on January 13, 2024. The bid opening will take place at the Junior High media center.

## Project Progress Photographs



Buggies and boards laid out in preparation for pouring concrete.



Vapor barrier laid down in preparation for pouring concrete.

## Project Progress Photographs






Concrete truck delivering concrete to west sided of building.



Concrete truck transferring concrete to a buggy.

## Project Progress Photographs

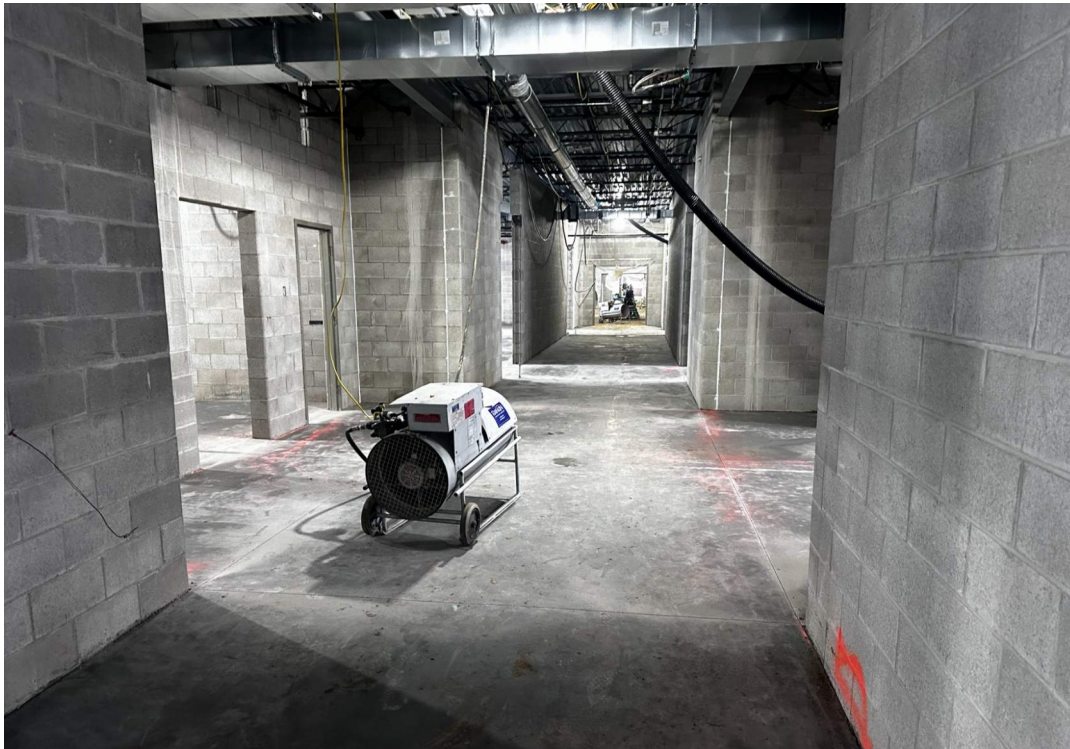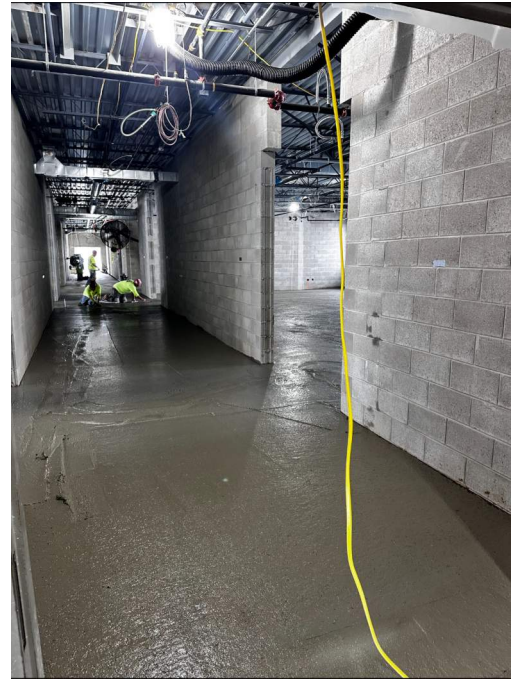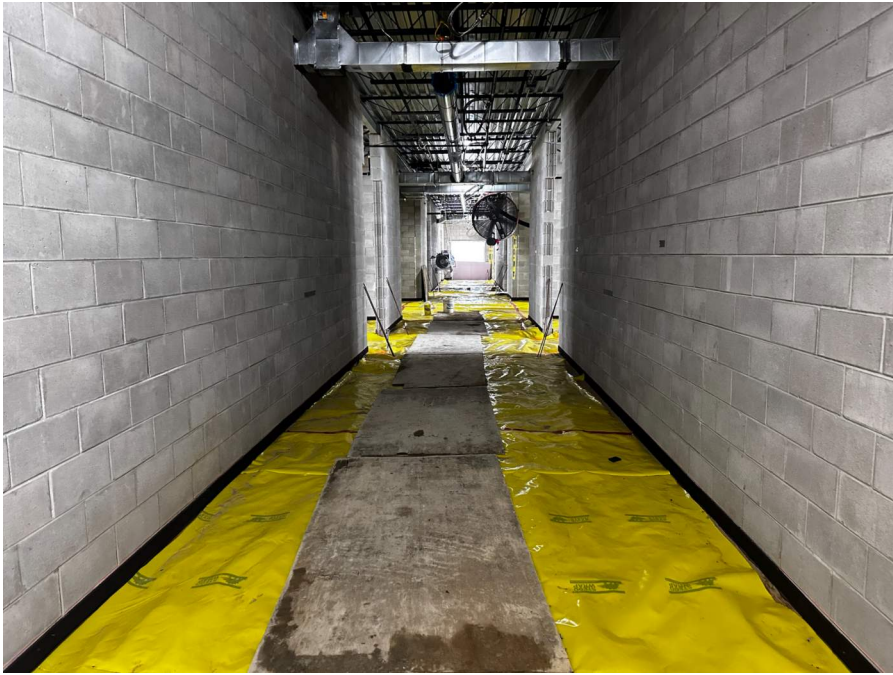

Stages of a concrete pour in hallway: Vapor barrier, leveling, and drying.

## Project Progress Photographs



Slab after sawcutting in classroom.



Hollow metal frame being installed in entryway.
