



FOWLERVILLE COMMUNITY
SCHOOLS



AUCH

Innovative Planners & Construction Managers
Builders Since 1908

i D S

Fowlerville Elementary School: Project Activities

- The punch list is wrapping up and site items are being completed as the weather allows.
- The concrete was installed at the receiving area.

HT Smith: Project Activities

- Playground equipment install continued.

HT Smith Schedule Status: Look Ahead

- Window shades and secure vestibule to be installed by mid-August.

High School: Project Activities

- VFD install began and piping insulation continued.
- Ceiling grid continued around the building in preparation for ceiling tile to be dropped.
- Lights were set back into the ceiling grid due to piping and duct completion.
- The CMU walls were completed, and the fence posts were set in concrete for the chiller enclosure.

High School: Look Ahead

- Switchgear and transformer install to be completed in mid-August.
- Chiller start up to take place in mid-August.

Natalie Kreeger: Project Activities

- Terminal unit install was completed, and piping was insulated in the classrooms.
- In the mezzanines, concrete pads were poured, air handling units were to begin piping and insulation.
- The fencing was completed at the chiller. Wire was pulled to the chiller and terminal units for power.
- Ceiling grid was installed.

Natalie Kreeger: Look Ahead

- Ceiling tile install to be completed by mid-August.
- Mechanical equipment and duct install to be completed in the mezzanines by mid-August.
- The drywall at the mezzanine masonry openings is to be completed by mid-August.

Junior High School: Project Activities

- The existing rooftop units were demoed, and beams were installed in the openings for the new rooftop units.
- The new rooftop units were set, and wire was pulled to them for power.
- Wire was run to the terminal units and ceiling grid was hung throughout the building.

Junior High School: Look Ahead

- The gas meters are to be upgraded by the end of August.
- RTU start up to take place in mid-August.

Munn: Look Ahead

- Munn will be demolished upon completion of the renovations at Smith.

Fowlerville Elementary: Project Progress Photos



Concrete that was installed at the receiving area and around the corner to the west.

HT Smith: Project Progress Photos



Age 2-5 playground equipment installed.



Shade and pour-in-place safety surfacing in toddler playground area.

Natalie Kreeger: Project Progress Photos



The chiller set on the east side of the building.



The new air handling unit in one of the three mezzanines.

Natalie Kreeger: Project Progress Photos



New transformer staged for install.



Demoed light pole after removal.

High School: Project Progress Photos



Chiller pads in preparation for enclosure and equipment setting.




Chiller enclosure progress including concrete masonry units and fencing poles.

Junior High School: Project Progress Photos



Duct openings being infilled with drywall.

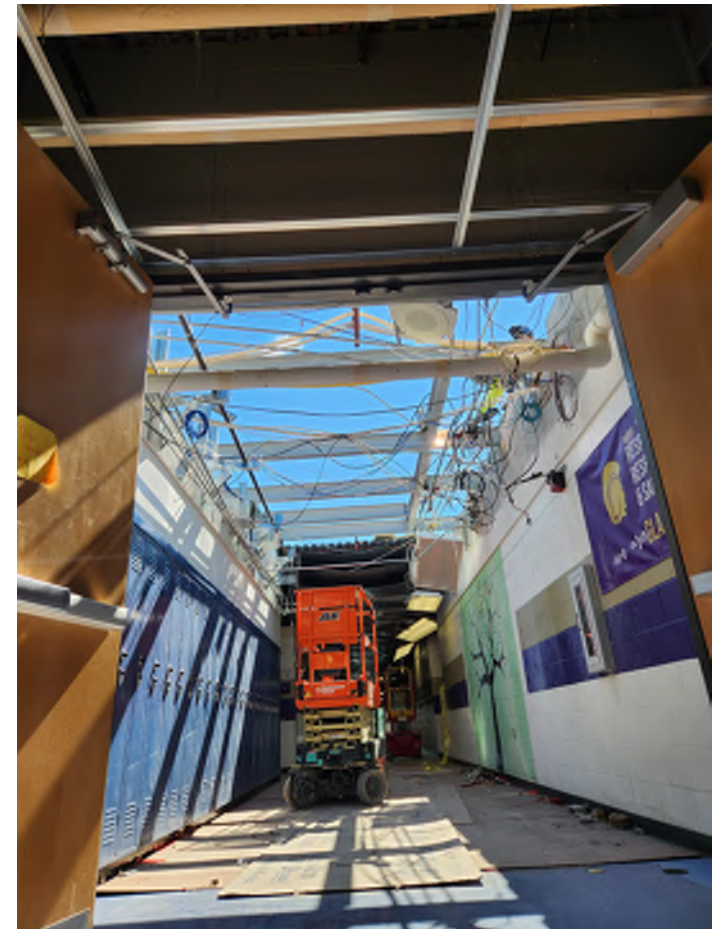

Deck opening in preparation for the support beams and rooftop unit curbs.

Junior High School: Project Progress Photos



Two of the seven new rooftop units set on the roof.

Junior High School: Project Progress Photos



Demoed rooftop equipment being lifted by a crane.

Junior High School: Project Progress Photos



Demoed rooftop mechanical equipment.



Rooftop unit curbs staged for install.
